

Create an inclusive environment that fosters discovery **Connect** our community with innovative opportunities **Inspire** lifelong learning and personal growth

Mission Statement for the Nevada County Community Library Strategic Plan 2017

POTENTIAL PHASES OF DISCOVERY AND DESIGN FOR TRUCKEE LIBRARY

VISION

Gensler

collect information from multiple sources to understand vision for Truckee Library

potential stakeholder groups

- administrators
- patrons
- students

potential exploration

- visual survey of existing spaces
- review of social media presence
- data mining (wifi, etc.)

PROGRAM

Gensler

understand your space needs both qualitatively and quantitatively

collect + analyze data

- develop spreadsheet to track existing and proposed space needs quantitatively
- process vision exploration to create a qualitative space needs program that captures aspirational program needs

one site visit for 3 people for vision and program

- 30 hours prep to visit
- 1 day meeting & travel: 20 hours
- Wrap up document and program tabulation: 60 hours

anticipated expenses:

- Flights \$600 each for three
- Hotel \$200 each for three for 2 nights
- Car Rental for one car \$300
- Airport Transportation for three \$300
- Meals for three \$300

line t

timeline 1-2 weeks

MASTER PLAN / CONCEPT DESIGN

Gensler + Your Local Architect

develop concept designs for Truckee space for implementation by your local Architect.

apply vision and program to space

- overlay space modifications onto existing space plans to illustrate renovations that will advance the vision and program
- work through 2-3 or more options and provide strength/weakness of each option to aid in decision-making process

understand budget

 work with a local contractor to price options to understand order of magnitude for each option

presentations will be via GoToMeeting web conferences

work with your local architect to be part of this process so that they can implement the strategy
120 hours

options: renderings \$2,000 each

timeline

1-4 weeks

DESIGN

CONSTRUCTION

Your Local Architect with Coordinated Reviews by Gensler

dependent on schedule, funding and approved master plan design and construction can proceed

(this is an optional add-on service if budget and time allows)

design and build the vision

 large scale or small scale projects to make impact and act on approved master plan

review of design drawings from your local architect, and provide some observation (via video conference) during construction.

40 hours

timeline4-5 weeks

timeline4-5 weeks

dependent on funding and schedule

40 hours @ 150/hr = **\$6,000**

timeline 2-4 weeks

4-10 week timeline

110 hours @ 150/hr = **\$16,500**

120 hours @ 150/hr = **\$18,000**

A TRANSFORMED LIBRARY ENVIRONMENT MAY LOOK LIKE...

(all Gensler projects shown)

Studio


Alone



Together

Space for the individual

Space for the team





Instruct


Instructive



Explorative

Lecture space

Creative space

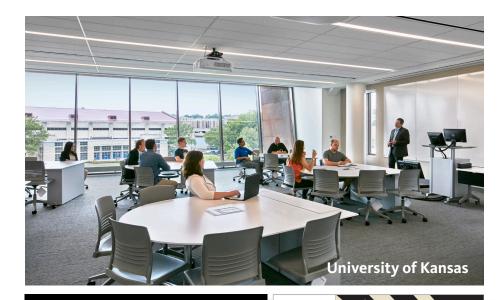



Library Programming

Create

Clean



Messy

Everything in its place

Maker space





thank you!
