



**HDR CCC Cost Proposal for
CM SERVICES FOR THE NEVADA COUNTY TRUCKEE RIVER BRIDGE PROJECT**

by Greg Zelss, February 19, 2024, Revised August 15, 2024

[illegible]

This Cost Proposal Assumes:

This Cost Proposal Assumes:

Does not include HDR's consultant team cost for work beyond HDR's control such as extra working days, claims, and rain days beyond the schedule shown above.

DOES NOT INCLUDE HOK'S CONSULTANT TEAM COST FOR WORK BEYOND HOK'S CONTROL SUCH AS EXAM WORKING DAYS, CLAIMS

Assumes that the NEVADA COUNTY Hirschdale Road Bridges Project is a 275 contractor working day contract.

Assumes that the NEVADA COUNTY Hillside Road Bridges Project is a 27.5 contract working day contract. Assumes that the Truckee River Bridge project and the Hinton Overhead (UPRR) Bridge Project will be managed simultaneously using the same contract Special Provisions Package.

Assumes CM contract administration files will be kept separately for federally funded contract administration audit purposes.


Assumes Contractor assumes that the Contractor does not work overtime and does not work on weekends. Cost proposal assumes that the Contractor works eight hours days Monday through Friday. This cost proposal assumes that the Contractor does not work overtime and does not work on weekends. Assumes Contractor assumes that the Contractor does not work overtime and does not work on weekends. Assumes Contractor assumes that the Contractor does not work overtime and does not work on weekends.

HDR rates are subject to up to a 4% annual merit increase beginning January 1 every year. Cost proposal assumes that the Contractor works eight hours a day Monday through Friday.

התאחדות המורים והמורות

Zeiss,

Greg P Date: 2024.08.15 13:19:35 -07'00'

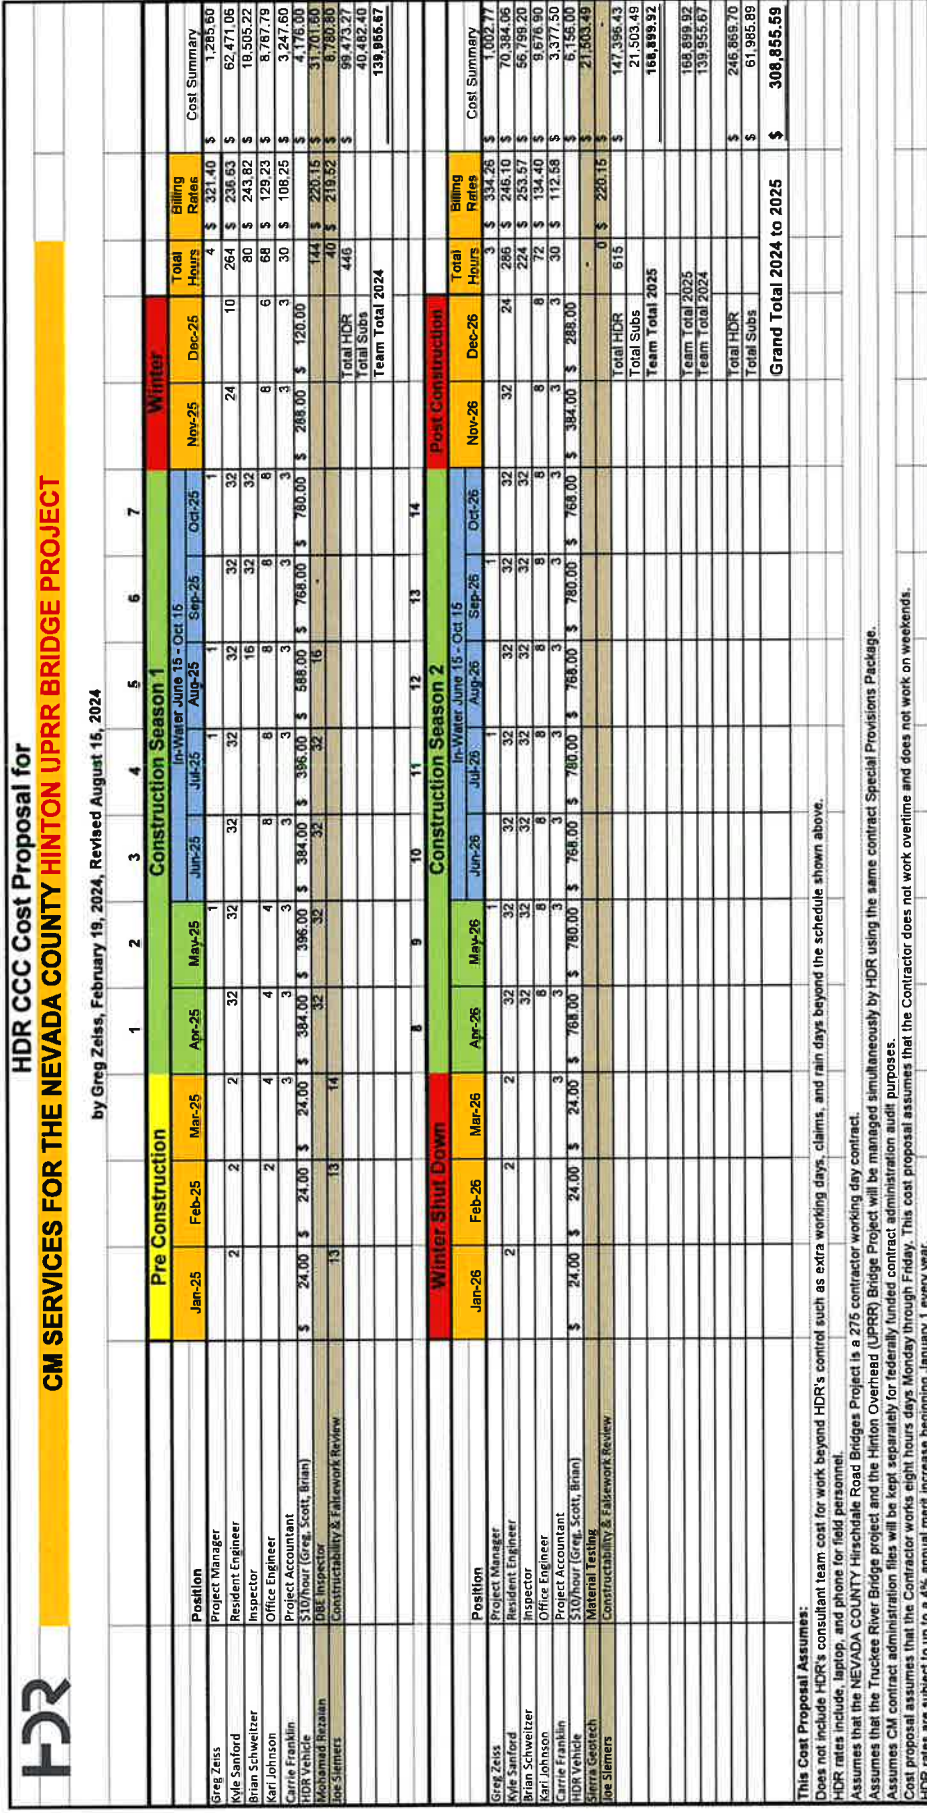

Does not include HDR's consultant team cost for work beyond HDR's control such as extra working days, claims, and rain days beyond the schedule shown above.

	HDR rates include laptop, phone for field personnel	
--	---	--

Assumes that the NEVADA COUNTY Hirschdale Road Bridges Project is a 275 contractor working day contract.

Assumes that the Truckee River Bridge project and the Hinton Overhead (UPRR) Bridge Project will be managed simultaneously by HDR using the same contract Special Provisions Package.

Assumes CM contract administration files will be kept separately for federally funded contract administration audit purposes

Cost proposal assumes that the Contractor works eight hours days Monday through Friday. This cost proposal assumes that the Contractor does not work overtime and does not work on weekends.

HRR rates are subject to up to a 4% annual merit increase beginning January 1 every year.

**Zeiss,
Greg P**
